

SIGN SCHEDULE



TRAFFIC CONTROL PERSON AHEAD



DUMPER TRUCK ACCESS SIGN
MONTHS 01 thru 04



WATCH FOR TRUCKS SIGN
MONTHS 01 TO 08



WORK AREA AHEAD
MONTHS 01 TO 16



WORKERS PRESENT SIGN
MONTHS 01 TO 06



NO PARKING SIGN
MONTHS 01 TO 16



PROPOSED CIRCULATION
MONTHS 01 TO 16



TEMPORARY PEDESTRIAN CROSSING
MONTH 16



TEMPORARY OCCUPATION
MONTHS 01 TO 14



TEMPORARY OCCUPATION
MONTH 16



BUILDING FOOTPRINT



LOADING AREA
MONTHS 01 TO 10



TEMPORARY FENCE
MONTHS 01 TO 16

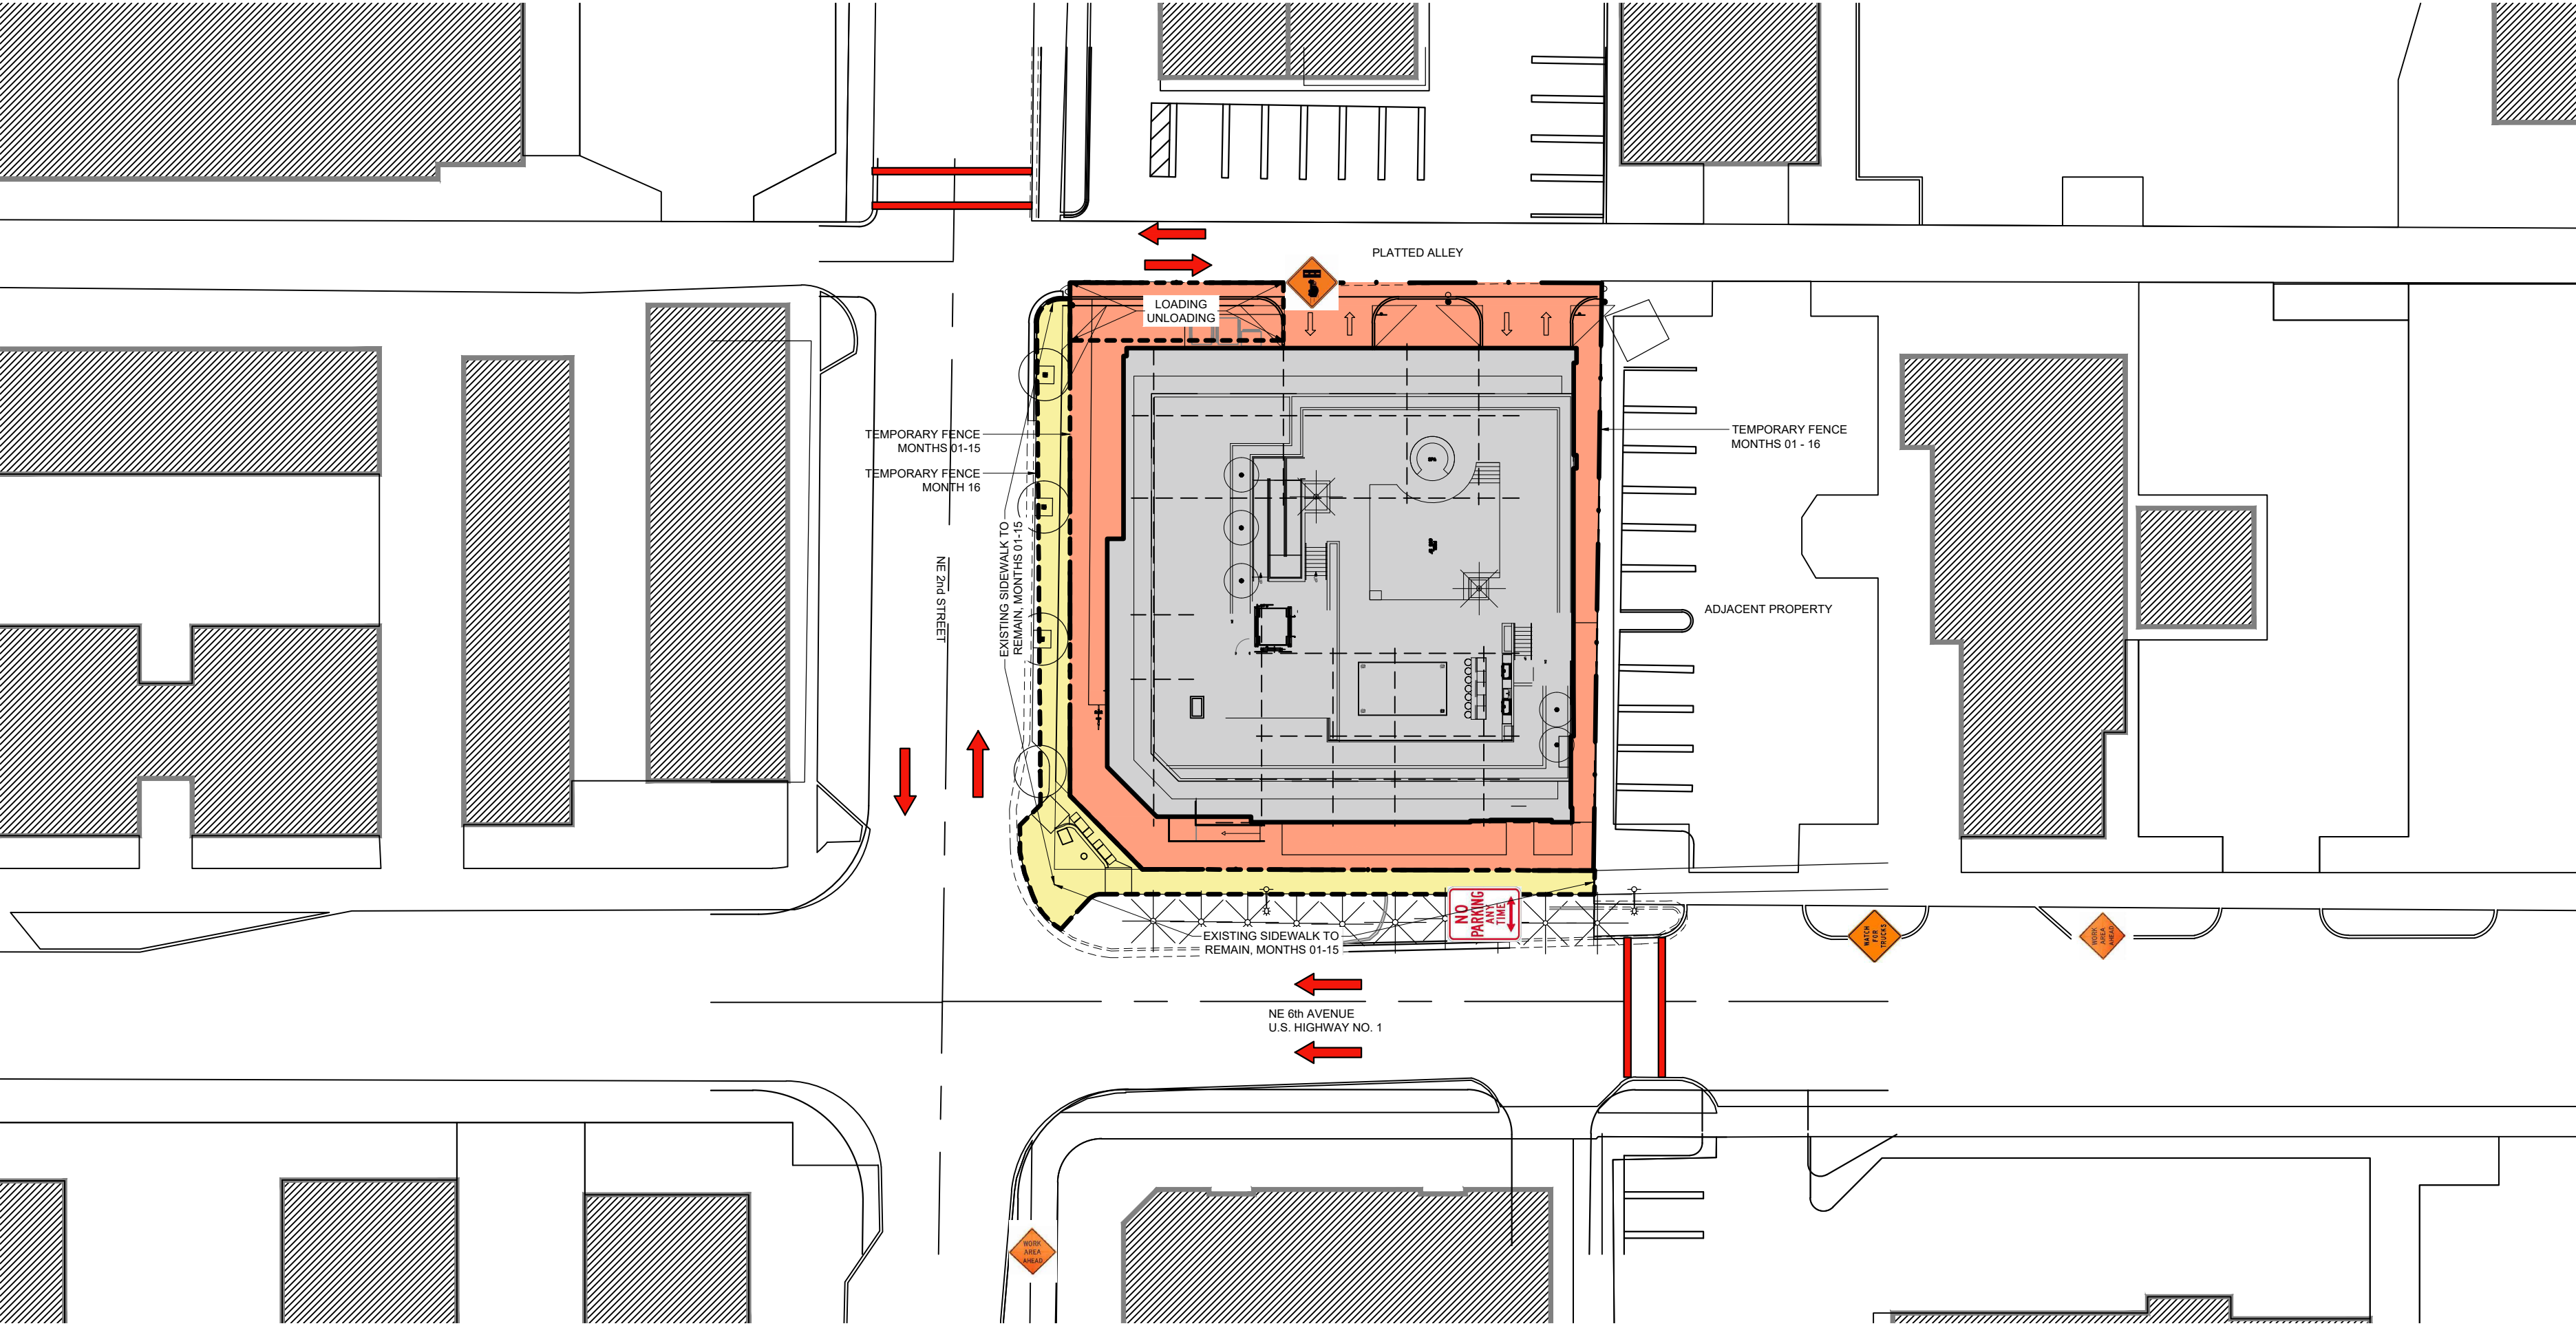


TABLE I - DEVICE SPACING

SPEED (MPH)	MAX. DISTANCE BETWEEN DEVICES			
	CONES OF TUBULAR MARKERS		TYPE I OR TYPE II BARRICADES OR VERTICAL PANELS OR DRUMS	
	25	50	25	50
25 OR LESS	25	50	30	50

DISTANCE BETWEEN SIGNS

SPEED (MPH)	SPACING (FT)		
	A	B	C
40 MPH OR LESS	200	200	200

NOTE:
1. SIDEWALK CLOSURE DURING MONTH 16 IS TO ENABLE THE CONSTRUCTION OF THE NEW PEDESTRIAN WALKWAY. MID BLOCK CROSSING IS PROVIDED FOR PEDESTRIANS TO SAFELY CROSS DURING THAT TIME.

BASIC CONSTRUCTION SCHEDULE

	MONTHS															
	01	02	03	04	05	06	07	08	09	10	11	12	13	14	15	16
DEMOLITION WORKS	█	█														
SITE WORK		█	█													
STRUCTURE			█	█	█	█	█									
MASONRY						█	█	█	█							
INTERIOR WALLS								█	█	█	█					
FINISHES									█	█	█	█	█	█	█	█
MEP							█	█	█	█	█	█				
SIGNS	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█
SIDEWALK RECONSTRUCTION																█
DUMPER TRUCKS ACCESS	█	█	█	█	█											
MIXER TRUCKS ACCESS		█	█	█	█	█										
LOADING / UNLOADING				█	█	█	█	█	█	█	█	█	█	█	█	█
ROAD WORKS / REPAVING															█	█

█ BUILDING WORK

█ PARKING LOT WORK

█ ROAD WORKS
