




Delray Beach Community Redevelopment Agency

June & July 2026 Monthly Work Plan Report

OVERVIEW

On September 30, 2025, the CRA Board of Commissioners adopted the Work Plan and Budget for Fiscal Year 2025-26. The Work Plan and Budget include projects and programs that emphasize the elimination of slum and blight through street beautification, improved mobility, preservation and development of affordable housing, commercial development, planning initiatives, historic preservation, and economic development initiatives within the CRA District which is divided into 8 Sub-Areas.

This report provides an overview of the status of the projects and programs in the Work Plan and other CRA activities within the CRA District Sub-Areas.

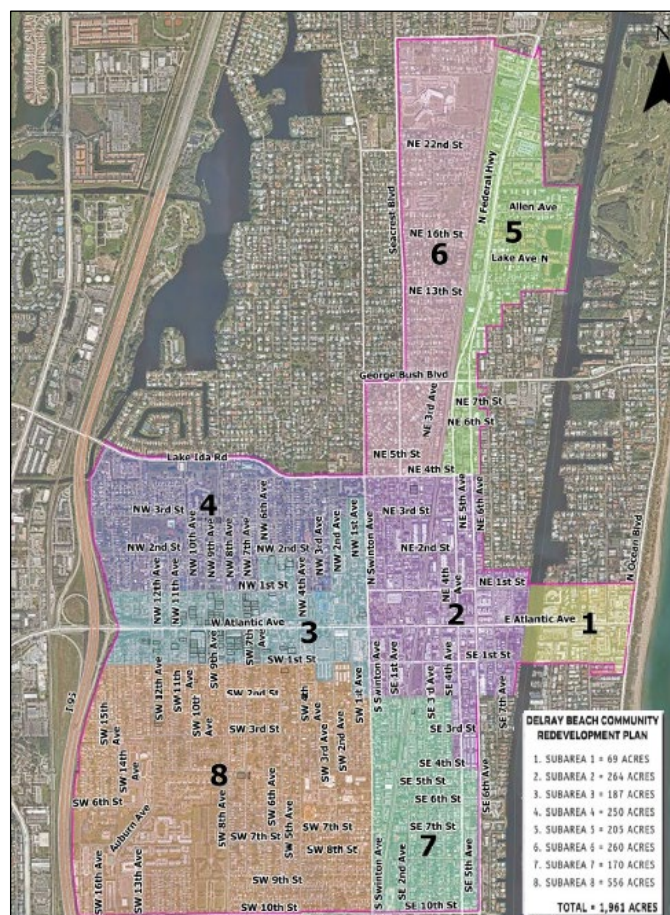

Overview of Projects by CRA Sub-Area

<u>Sub-Area 1</u> N/A	<u>Sub-Area 5</u> N/A
<u>Sub-Area 2</u> • Implementation of Old School Square Master Plan (CIP) • Crest Theatre Historic Preservation Improvements – Architectural Services (CIP) • 313 NE 3rd Street – Exterior and Interior Repairs	<u>Sub-Area 6</u> N/A
<u>Sub-Area 3</u> • 95 SW 5th Avenue Development • NW 600 Block Redevelopment • NW 800 Block Redevelopment • 182 NW 5th Avenue – Interior Repairs • 20 N Swinton Avenue Maintenance • West Atlantic Avenue Redevelopment: • Northwest: 900 and 1000 Blocks • Southwest: 600, 700, 800, 900, 1000, 1100 and 1200 Blocks • 102 NW 5th Avenue – Exterior and Interior Renovations	<u>Sub-Area 7</u> • 235 SE 2nd Avenue - Demolition
<u>Sub-Area 4</u> • Pompey Park Construction (CIP) • NW Neighborhood Infrastructure Improvements (CIP) • 111 NW 11th Avenue - Demolition	<u>Sub-Area 8</u> • Carver Square Park (CIP) • Merritt Park – Shade Enhancement (CIP) • SW 8th Avenue and SW 2nd Street Improvement (intersection) (CIP) • SW 8th Avenue Streetscape Improvements (CIP)
<u>Projects in Multiple Sub-Areas</u>	
<u>Sub-Areas 1-8</u> • Land Acquisition • CRA Redevelopment Plan Amendment • Palm Tree Replacement	

Redevelopment and Capital Improvements Projects

CRA Managed

Project Name	Phase	CRA Sub-Area	Update
95 SW 5 th Avenue Development <u>CRA GL #: 6208D</u>	Construction	3	<u>Contract with Ahrens Companies (GC) Approved:</u> 1-24-23. A groundbreaking ceremony on 7-12-23 was well attended. Final elevator and fire inspections completed. Pending final project close-out punch list.
NW 600 Block Redevelopment <u>CRA GL #: 5123</u>	Design	3	FLUM and Rezoning Approved. <u>CRA Conceptual Design:</u> CRA Board: Selected Site Plan Option A. <u>Architectural and Design Services:</u> RFQ: Published: 3-8-21. RFQ awarded at the 8-31-21 CRA Board meeting. CRA Board approved agreement between Synalovski, Romanik and Saye Architects and CRA at the 11-26-23 CRA Board Meeting. Consultant is working on development options, and meetings with City staff are scheduled to discuss preliminary concerns and questions. An update on the designs was provided at the CRA Workshop on 10-29-24. A CRA social event held on 12-5-24 was well attended in which the community provided input about this project. Consultant is working on updated designs and having meetings with City staff. <u>Commercial project:</u> Consultant is addressing City staff review comments related to the site plan submittal. <u>Residential project:</u> Consultant is working with City staff to coordinate project work with the NW Neighborhood Infrastructure Improvements. Consultant is addressing City staff review comments related to the site plan submittal. <u>Hatcher Construction Project:</u> Conditional Use: Approved 1-5-2021. Site Plan Approved: 2-10-21. Easements, right of way deed and landscape maintenance agreement approved: 4-6-21. At the 7-15-21 CRA Board Meeting, CRA Staff presented a purchase and sale agreement (PSA) to the Board. Hatcher and CRA staff are finalizing details of the PSA. Building Permit Application approved in October. At the 10-20-21 CRA Board Meeting, CRA Board approved a Loan Commitment Letter to provide Hatcher a \$1.4 million loan from the CRA to bridge their private financing gap. Construction commenced. The Groundbreaking ceremony on 12-9-21 was well attended. A ribbon cutting ceremony on 12-6-23 was well attended. Hatcher moved to the new offices and the first tenant moved in June, 2024. A second tenant moved in January 2026. A ribbon cutting ceremony was well attended.

NW 800 Block of West Atlantic Avenue <u>CRA GL #: 5124</u>		3	<u>805 W. Atlantic Ave. Site:</u> Consultant is working on delineating the plume. A remediation process will follow. Pending State/County determination of median remediation – August 2025 plume delineation work began. Site will be part of the RFP for the NW 800 Redevelopment Block. <u>Conceptual Design:</u> CRA Board approved the proposed next steps at 1-25-22 CRA Board Meeting. CRA staff and consultant are working on the next tasks. CRA Board approved the final conceptual design presented at the 9-29-22 CRA Board Meeting. CRA staff issued a Request for Qualifications (RFQ) with the following dates: RFQ Issued: October 4, 2024. A voluntary pre-proposal meeting was scheduled on October 18, 2024. Questions submittal deadline on November 13, 2024. Submission Deadline: December 18, 2024. 3 proposals were received. CRA Board approved the cancelation of the proposals received and directed staff to reissue the RFQ. RFQ Issued: January 30, 2025. A voluntary pre-proposal meeting was scheduled for February 12, 2025. Questions submittal deadline: February 21, 2025. Submission Deadline: March 18, 2025. Selection committee meeting: June 12, 2025 CRA Board workshop and presentations from all bidders: October 7, 2025. At the November 2025 CRA Board meeting, the CRA Board canceled the RFQ and rejected all proposals received. CRA staff has engaged JLL to conduct a market sounding for CRA-owned West Atlantic Avenue properties. The results of the market sounding will help guide a future Request for Proposals (RFP). At the CRA Board Especial meeting on May 13, the unsolicited proposal was presented and the public and CRA Board provided comments. There will be a future CRA Board Especial meeting to follow up on the comments received. CRA staff is researching the ROW abandonment issue and what would be needed for the future development of NW 800 Block.
182 NW 5 th Avenue – Interior Repairs <u>CRA GL #: TBD</u>	Design	3	The repair work will restore the interior of the building to its original state. Consultant and CRA staff are working to finalize design and construction documents that will be included with the ITB.
20 N Swinton CRA Office – Exterior and Interior Repairs <u>CRA GL #: 8405</u>	Design	3	The repair work will include repairing the roof, siding, and HVAC. Consultant and CRA staff are finalizing the design and construction documents that will be included with the ITB.
313 NE 3 rd Street – Exterior and Interior Repairs <u>CRA GL #: 7450</u>	ITB	2	The repair work includes the roof, gutters, and interior concrete flooring. ITB Issued: July 3, 2025. A voluntary pre-proposal meeting: July 15, 2025.

			Questions submittal deadline: July 25, 2025. Bid submission deadline: August 20, 2025. A construction services agreement with Waypoint Contracting, Inc. was approved at the January 27, 2026, CRA Board meeting. NTP issued on 2/26/26. Work inside the building is in progress.
235 SE 2nd Avenue – Property Demolition <u>CRA GL #: 5613</u>	Planning	7	The Solid Waste Authority Board awarded a grant to demolish the property. CRA staff is working with Palm Beach County to receive grants related to the pre-demolition asbestos survey and additional assessments through the Environmental Protection Agency Assessment Grant. Asbestos survey, GPR Survey and preliminary soil testing have been completed. CRA staff is reviewing asbestos abatement and demolition proposals.
111 NW 11th Avenue – Property Demolition <u>CRA GL #: 5613</u>	Planning	4	The Solid Waste Authority Board awarded a grant to demolish the property. CRA staff is reviewing proposals to start the demolition permit process.
CRA Redevelopment Plan Amendment <u>CRA GL #: 8409</u>	Planning – 50%	1-8	CRA Board approved the resuming of the project at 1-25-22 CRA Board Meeting. Interviews are completed. An agenda item was presented at the CRA Board meeting on 8-29-24 to request Board input on the draft report. CRA staff and consultant are working on a final draft report. An agenda item will be discussed at the July CRA Board meeting. https://www.surveymonkey.com/r/CRAPlanSurvey
West Atlantic Avenue Redevelopment: • Northwest: 900 and 1000 Blocks • Southwest: 600, 700, 800, 900, 1000, 1100 and 1200 Blocks <u>CRA GL #: TBD</u>	Planning	3	At the September CRA Board meeting, CRA staff presented an agenda item regarding the Request for Proposals for the SW 600 Block. At the November CRA Board meeting, CRA Board approved a work assignment to conduct a “market sounding”. CRA staff has engaged JLL to conduct a market sounding for CRA-owned West Atlantic Avenue properties. The results of the market sounding will help guide a future Request for Proposals (RFP). <u>SW 600 Block:</u> At the CRA Board Especial meeting on May 13, the unsolicited proposal was presented and the public and CRA Board provided comments. There will be a future CRA Board Especial meeting to follow up on the comments received. <u>SW 700 and 800 Blocks:</u> An agenda item will be discussed at the July CRA Board meeting.
Land Acquisition <u>CRA GL #: 5610</u>	Planning	1-8	CRA staff continues working on land acquisition efforts throughout the CRA District.
102 NW 5th Avenue – Exterior and Interior Renovations <u>CRA GL #: TBD</u>	Planning	3	Work to include interior renovations of all units as well as reconstruction of the parking lot. Consultant and CRA staff are working to finalize design and construction documents that will be included with the ITB.

Projects Completed

Historic Wellbrock House Relocation <u>CRA GL#: 8405</u>	Corey Jones Isle Replat (Lot 1 and Lot 2) <u>CRA GL#: 6621</u>
Historic Wellbrock House Local Historic Designation <u>CRA GL#: 8405</u>	NW 600 Block Future Land Use Map Amendment and Rezoning <u>CRA GL#: 5120</u>
Historic Wellbrock House Certified Site Plan Approval <u>CRA GL#: 8405</u>	<u>Rev. J.W.H. Thomas Jr. Park – Landscaping Upgrades</u> <u>SWA Grant</u>
Corey Jones Isle Workforce Housing <u>CRA GL#:6621</u>	98 NW 5 th Avenue Renovation – Certified Site Plan Approval <u>CRA GL #: 6208</u>
95 SW 5 th Avenue Design – Certified Site Plan Approval <u>CRA GL #: 6214</u>	34 NW 6 th Avenue – Property Demolition <u>CRA GL #: 6214</u>
Historic Wellbrock House - Historic Preservation <u>CRA GL #: 8405</u>	Historic Wellbrock House - Historic Preservation Project <u>CRA GL #: 8405</u>
<u>Rev. J.W.H. Thomas Jr. Park - SWA Grant</u> <u>CRA GL #: 5366</u>	606 W. Atlantic Avenue (Schuler's) – Property Demolition <u>SWA Grant</u> <u>CRA GL #: 5123</u>
Carver Square <u>CRA GL #: 6621</u>	250 NW 8 th Avenue -Property Demolition <u>CRA GL #: TBD</u>
324 & 325 NE 3 rd Ave/Water Main Infrastructure Improvement Grant <u>CRA GL #: 5251</u>	Fixed-Route Transportation Services <u>CRA GL #: 5320</u>
Point-to-Point Transportation Services (Transferred) <u>CRA GL #: 5320</u>	98 NW 5 th Avenue Renovation <u>CRA GL #: 6208</u>
700 W. Atlantic Avenue – Property Demolition <u>CRA GL #: TBD</u>	27 NW 7 th Ave – Parking Demolition <u>CRA GL #: TBD</u>
102 NW 5 th Avenue – Exterior Repairs <u>CRA GL #: 6222</u>	Set Transformation Plan Update <u>CRA GL #: TBD</u>

City Managed

Project Name	Phase	CRA Sub-Area	Percentage Complete	Update
NW Neighborhood Infrastructure Improvements <u>City Project #: 17-020</u> <u>CRA GL #: 5622</u>	Pre-Construction	4	N/A	<u>Design Services:</u> 100% Design plans for Phase 1 were submitted to City in June 2025. Owner's Representative has reviewed 100% plans for all three phases. Waiting for CMAR to come on board tentatively in April/May 2026. At that time, Plans will be reviewed for QAQC with the designer, Owner's Rep. and City staff. <u>Construction:</u> City issued CMAR RFQ Solicitation advertised December 18, 2024. The committee scoring meeting was held on Friday May 30th, 2025. Construction Manager at Risk for Phase I was awarded to Kiewit Corporation, on 4-7-26. <u>Owner's Representative:</u> Owner's Representative was awarded to Holtz Consulting Engineers, Inc. on 10-14-25. City staff held a Notice to Proceed meeting with the CMAR Company and the Owner's Representative to address QA/QC requirements, finalize the design, and negotiate the construction cost for the project -Guaranteed Maximum Price (GMP). City staff and consultants continue to review the design plans through several QA/QC review meetings, including review of the design plans, decorative lighting layout and relocations, right-of-way (R/W) deeds, and other preconstruction coordination items. Phase 2 negotiations have begun. Once the GMP has been finalized and negotiations are complete, the Phase 2 construction contract must be presented to the City Commission for approval before construction can begin. Additional information is available on the website: http://nwneighborhoodproject.com/
Pompey Park Construction <u>City Project #: 16-102</u> <u>CRA GL #: 5661</u>	Pre-Construction	4	N/A	A project kick-off meeting for Phase 1 Pre-construction services was conducted on 7/1/25. The 1st outreach event (public and vendors/trades) was conducted on 9/10/25. The GMP solicitation was advertised on 12/2/25 and subcontractor bids were received/opened on 1/30/26. The draft GMP, currently being negotiated, includes various scope options related to the available project budget. GMP will be presented to CRA Board/Commission for

				consideration in May 2026. Construction is anticipated to begin around June/July 2026. At the June 9, 2026, City Commission meeting, there was consensus to move forward with the GMP and bring it to City Commission for approval.
Palm Tree Replacement <u>CRA GL #: 7335</u>		1-8	N/A	Solicitation opened: April 2, 2025, at 2:00pm for two (2) weeks. Solicitation closes on April 16, 2025, at 2:00pm. Solicitation to be re-opened, Purchase Department is currently drafting the ITB. •Solicitation was put out for advertisement on June 4, 2025. •The Pre-Proposal Conference/Site Visit was scheduled for June 17, 2025, at 10:00 a.m. •Solicitation deadline is on June 30, 2025, at 2:00 p.m. A bidder was not selected. Working with a consultant to edit the scope of work. Due to challenges in identifying a vendor qualified to complete the scope of work, the work will be completed under a citywide tree trimming and pruning RFP.
SW 8th Avenue and SW 2 nd Street Improvement (intersection) <u>CRA GL #: 5367</u>	Design	8	100%	Design plans are 100% done, and construction is expected to begin at the end of March 2026. The contractor started with the survey of the Southwest corner on March 12 th . Construction is anticipated to begin on 8/1/26. MOT documents will be included in the July 14 th City Commission agenda for the road closure during the demolition and construction of the intersection. Construction will take approximately 6 to 8 weeks, weather permitting, to allow the demolition of the roundabout and installation of a new raised intersection.
SW 8 th Avenue Streetscape Improvements <u>CRA GL #: 5368</u>	Design	8	30%	The primary goal of the project is to include upgrades to water, sewer, stormwater, roadway, sidewalks, traffic calming and lighting. The initial project includes design/construction of roadway and drainage improvements on SW 8th Avenue between SW 4th Street and SW 10th Street and pervious concrete paving on the alley from SW 1st Street to SW 2nd Street, between SW 9th Avenue and SW 10th Avenue. Notice to proceed issued on 1-15-26. Survey work is completed. Design is expected to begin in April. Design work just started and is approximately 10% complete. 30% Design documents has been completed. QA/QC review was completed jointly by City staff and consultant in June. The project is moving towards the 60% Design phase.
Implementation of Old School Square Master Plan <u>CRA GL #: 5201</u>	Planning	2	N/A	Scope of work was determined to include new lights and updated curtain roll-ups. Public Works issued an NTP for design work on 2/9/26. The City and Consultant will have a field meeting to discuss where to install the new lighting and share ideas about the roll-ups by the arches. The Architect is finalizing the design. The lighting and new gates for the arches are currently in the design phase. Applications have been submitted to the Historic Board, and the consultant is obtaining quotes for the fabrication of the new gates for the arches. Consultant is finalizing the design, cost estimate and specifications for submittal to the Historic Board.

Crest Theatre Historic Preservation Improvements – Architectural Services <u>CRA GL #: 5203</u>	Planning	2	N/A	The primary goal of this project is to renovate and modernize the interior of Crest Theatre. A meeting with the design team was scheduled for 10/2/25. Design team was scheduled to conduct a site assessment on 10/9/25. Design team presented conceptual options at 12/12/25 meeting. Updated options and cost estimates were presented to City staff at 1/14/26 meeting. Design team presented options to City Commission on 2/3/26 and is working on the final report and a proposal for the final design based on the input by City Commission. A revised proposal was expected in April 2026. The agreement for the final design was approved by City Commission in May and a revised PO issued in June.
--	----------	---	-----	--

Projects Completed

SW 3 rd Court, SW 4 th Street, SW 6 th Street, and SW 7th Avenue <u>City Project #: 17-108</u> <u>CRA GL #: 5351</u>	NE 3rd Street Improvements <u>City Project #: 11-024</u> <u>CRA GL #: 5251</u>
Osceola Park Neighborhood Imp. Phase I <u>City Project #: 16-095</u> <u>CRA GL #: 5510</u>	Artists Alley Drainage Improvement <u>City Project #: TBD</u> <u>CRA GL #: 5625</u>
SW Neighborhood Alleys – 3 Alleys <u>City Project #: 17-103</u> <u>CRA GL #: 5361</u>	Osceola Park Neighborhood Imp. <u>City Project #: 16-095</u> <u>CRA GL #: 5510</u>
Currie Commons Restrooms <u>City Project #: TBD</u> <u>CRA GL #: 5525</u>	Carver Square Park <u>City Project #: TBD</u> <u>CRA GL #: 5364</u>
Merritt Park – Shade Enhancement <u>City Project #: TBD</u> <u>CRA GL #: 5621</u>	Wayfinding Signage <u>CRA GL #: 5236</u>
