




Delray Beach Community Redevelopment Agency

October 2021 Monthly Work Plan Report

OVERVIEW

On September 28, 2021, the CRA Board of Commissioners adopted the Work Plan and Budget for Fiscal Year 2021-22. The Work Plan and Budget include projects and programs that emphasize the elimination of slum and blight through street beautification, improved mobility, preservation and development of affordable housing, commercial development, planning initiatives, historic preservation, and economic development initiatives within the CRA District which is divided into 8 Sub-Areas.

This report provides an overview of the status of the projects and programs in the Work Plan and other CRA activities within the CRA District Sub-Areas.

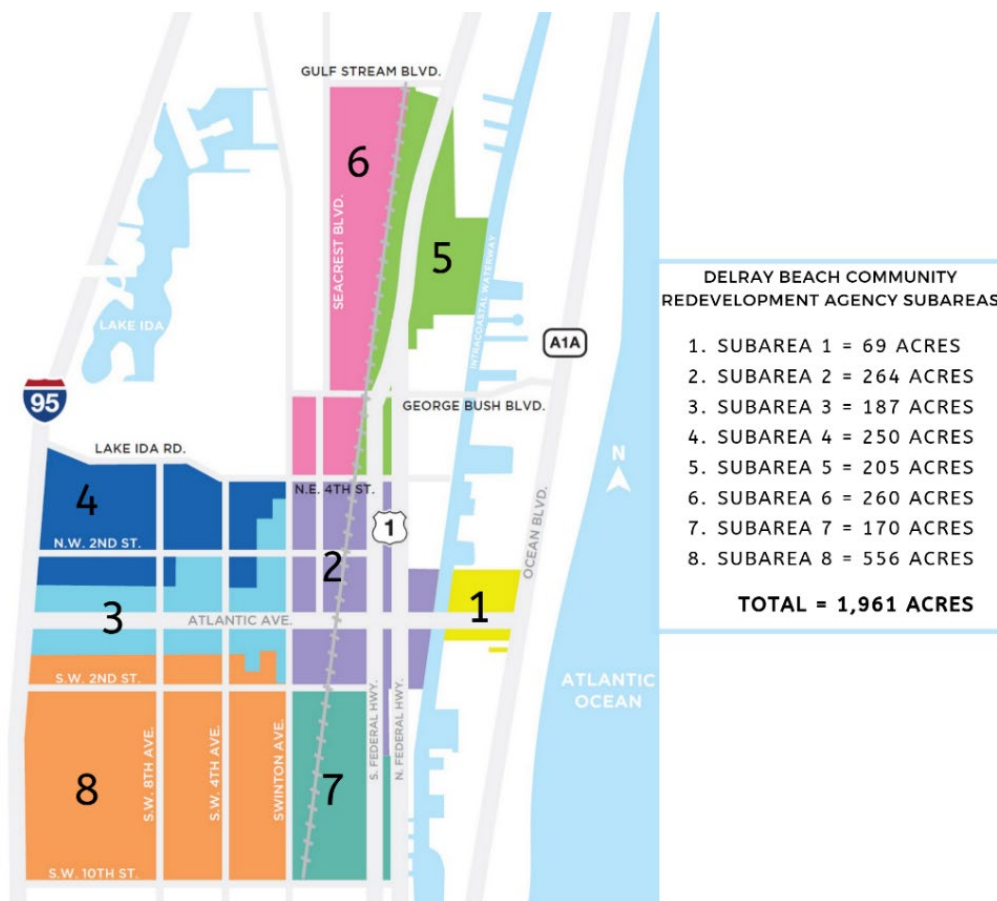

<u>Overview of Projects by CRA Sub-Area</u>	
<u>Sub-Area 1</u> N/A	<u>Sub-Area 5</u> N/A
<u>Sub-Area 2</u> • N/A	<u>Sub-Area 6</u> N/A
<u>Sub-Area 3</u> <ul style="list-style-type: none"> • SW 600-800 W. Atlantic Avenue Development • NW 600 Block Redevelopment • NW 800 Block Redevelopment • 98 NW 5th Avenue Rehabilitation • 95 SW 5th Avenue Development • 22 N. Swinton Avenue Rehabilitation 	<u>Sub-Area 7</u> <ul style="list-style-type: none"> • Osceola Park Neighborhood Imp. (CIP)
<u>Sub-Area 4</u> <ul style="list-style-type: none"> • NW Neighborhood Improvements (CIP) • Pompey Park 	<u>Sub-Area 8</u> <ul style="list-style-type: none"> • SW 3rd Court, SW 4th Street, SW 6th Street, and SW 7th Avenue (CIP) • SW Neighborhood Alleys (CIP) • Carver Square Workforce Housing • Rev. J.H.W Thomas Jr. Park
<u>Projects in Multiple Sub-Areas</u>	
<u>Sub-Areas 1-8</u> <ul style="list-style-type: none"> • Connect Delray Beach - Freebee • Wayfinding Signage • CRA Redevelopment Plan 	

Redevelopment Projects/Improvements

Project Name	Phase	CRA Sub-Area	Update
Request for Proposals 600-800 Blocks of W. Atlantic Avenue – BH3 Management, LLC	N/A	3	<u>Small Scale Land Use Map Amendment and Rezoning</u> : The CRA Board approved a Fourth Amendment to the PSA on 2-23-21. The CRA Board approved to Terminate the PSA on 7-15-21. Formal notice has been provided.
98 NW 5 th Avenue Renovation <u>CRA GL #: 6208</u>	Design	3	<u>Class III (Site Plan) and Waiver request</u> : Received Historic Preservation Board and City Commission Approvals. <u>Site Plan Certification Submitted</u> : 2-22-21. Pending Approval. <u>Right of Way Dedications</u> : City Commission Approved: 10-5-21. <u>Easements & Agreements</u> : City Commission Approved: 10-5-21. <u>Building Permit</u> : 8-18-21. Technically Approved. ITB: CRA Board Awarded: 5-25-21 to Waypoint Contracting, Inc. Pending executed contract.
95 SW 5 th Avenue Design <u>CRA GL #: 6214</u>	Design	3	<u>Downtown Development Authority Board</u> : Approved. <u>Waiver Request</u> : SPRAB: Approved 4-28-21. <u>City Commission (Waiver)</u> : Approved: 5-18-21. <u>Class V (Site Plan)</u> : SPRAB: Approved 8-25-21. <u>Easements & Agreements</u> : Pending Documents. <u>Site Plan Certification</u> : Submittal Pending. <u>Construction Documents</u> : Consultant Preparing. <u>Building Permit Submittal</u> : Pending. ITB: TBD.
Carver Square <u>CRA GL #: 6621</u>	Design	8	<u>Bid #CRA No. 2020-01 Development & Disposition of Properties RFP</u> : Awarded to Pulte Home Company: 1-26-21. The CRA Board Approved the Agreement: 4-27-21. <u>Purchase & Sale Agreement</u> : Entered into Agreement: 5-4-21. <u>Ratification 1st Amendment</u> : CRA Board Approved: 7-15-21. <u>First Amendment to the Agreement</u> : Ratification the First Amendment on 7-15-21. <u>Building Permits for 20 SF Homes</u> : In Review. <u>Developer to provide update to CRA Board</u> : 10-20-21.
Historic Wellbrock House Historic Preservation Project <u>CRA GL #: 8405</u>	Design	3	<u>Class IV (Site Plan) request</u> : <u>Downtown Development Authority</u> : Approved. <u>Historic Designation</u> : Approved. <u>Site Plan</u> : Received Historic Preservation Board Approval. <u>Site Plan Certification</u> : Approved: 3-5-21. <u>Interior/Exterior Renovation</u> : <u>Construction Documents</u> : Technically complaint (April). Pending GC to issue permit. ITB: CRA Board Awarded: 8-31-21 to Waypoint Contracting, Inc Pending executed contract.
NW 600 Block Redevelopment <u>CRA GL #: 5120</u>	Conceptual Design	3	FLUM and Rezoning Approved. <u>CRA Conceptual Design</u> : CRA Board: Selected Site Plan Option A. <u>Architectural and Design Services</u> : RFQ: Published: 3-8-21. RFQ awarded at the 8-31-21 CRA Board meeting. Pending executed contract.

			<u>Hatcher Construction-Ground Lease Conceptual Design</u> : Conditional Use: Approved 1-5-2021. Site Plan Approved: 2-10-21. Easements, right of way deed and landscape maintenance agreement approved: 4-6-21. Building Permit Application submitted to the Building Department and in review. Applicant is addressing comments from the review. At the 7-15-21 CRA Board Meeting, CRA Staff presented a purchase and sale agreement (PSA) to the Board. Hatcher and CRA staff are finalizing details of the PSA.
<u>NW 800 Block of West Atlantic Avenue</u> <u>CRA GL #: 5124</u>	Conceptual Design	3	<u>Site</u> : Limerock removed: 8-23-21. Fence removal and sod installation to be completed by the end of October. <u>Conceptual Design</u> : Two public outreach meetings were held at Pompey Park to receive input from the community.
<u>Rev. J.W.H. Thomas Jr. Park</u> <u>SWA Grant</u> <u>CRA GL #: 5366</u>	Design		<u>Site Plan Amendment</u> : New playground equipment installation: Submitted an application to the City Development Services Department for a pre-application meeting to discuss scope. Development Services Director determined project could go straight to Building Permit. Coordinating permit to construct with Vendor/Contractor.

Projects Completed

<u>Historic Wellbrock House Relocation</u> <u>CRA GL#: 8405</u>	<u>Corey Jones Isle Replat (Lot 1 and Lot 2)</u> <u>CRA GL#: 6621</u>
<u>Historic Wellbrock House Local Historic Designation</u> <u>CRA GL#: 8405</u>	<u>NW 600 Block Future Land Use Map Amendment and Rezoning</u> <u>CRA GL#: 5120</u>
<u>Historic Wellbrock House Certified Site Plan Approval</u> <u>CRA GL#: 8405</u>	<u>Rev. J.W.H. Thomas Jr. Park – Landscaping Upgrades</u> <u>SWA Grant</u>
<u>Corey Jones Isle Workforce Housing</u> <u>CRA GL#:6621</u>	

Capital Improvement Projects

CRA Managed

Project Name	Phase	CRA Sub-Area	Percentage Complete	Update
CRA Redevelopment Plan Amendment <u>CRA GL #: 8409</u>	N/A	1-8	N/A	On 6-23-20, the CRA Board approved a pause due to the nature of the project and the concerns surrounding public gatherings in light of the COVID-19 pandemic. CRA Staff will discuss this project at a future meeting.
Point-to-Point Transportation Services <u>CRA GL #: 5320</u>	N/A	1-8	N/A	At the CRA Board Meeting on 8-31-21, the CRA Board approved the renewal of the contract on a month-to-month basis. CRA staff will meet with City staff to continue working on transferring the service. Freebee continues to reach out to local and non-local businesses to advertise on Freebee vehicles. Regular service hours and safety precautions for the drivers and riders are still in effect. Additional information is available on the website: https://delraycra.org/transportation/
SW Neighborhood Alleys <u>City Project #: 17-103</u> <u>CRA GL #: 5361</u> <u>CIP Proj. Map #: 7</u>	3 Alleys – Design	8	N/A	3 Alleys – CRA staff is exploring options on how to approach the alley improvements.

Projects Completed

324 & 325 NE 3 rd Ave/Water Main Infrastructure Improvement Grant <u>CRA GL #: 5251</u>	Fixed-Route Transportation Services <u>CRA GL #: 5320</u>
---	--

Capital Improvement Projects

City Managed

Project Name	Phase	CRA Sub-Area	Percentage Complete	Update
NW Neighborhood Improvements City Project #: 17-020 CRA GL #: 5622	Design	4	N/A	<p>Craig A. Smith & Associates (CAS) was awarded an agreement for the design of the NW Neighborhood Improvements for \$1,590,860.00.</p> <p>-CAS and the City had meeting on comments for QA/QC the conceptual design report: 10-1-20. Final Report to City on November 13.</p> <p><u>Design Services:</u> City is taking RFQ to award project on November 2021. Additional information is available on the website: http://nwneighborhoodproject.com/</p>
SW 3rd Court, SW 4th Street, SW 6th Street, and SW 7th Avenue City Project #: 17-108 CRA GL #: 5351	Construction	8	Construction – 90%	<p><u>Baxter Woodman</u> was awarded an agreement for construction, engineering and inspection services (CEI) for \$587,416.00.</p> <p><u>Ric-Man</u> was awarded an agreement for general contractor construction services (GC) for \$5,648,785.00. Project commenced in June. Monthly project status: Additional information is available on the website: <u>October Work Schedule:</u> -Sod and Landscaping continuing installation. -Final asphalt lift. http://sw4thstreet.com/ Social Media Page Links Below: https://www.facebook.com/SW4thStreet/ https://twitter.com/sw4th</p>
Osceola Park Neighborhood Imp. City Project #: 16-095 CRA GL #: 5510	Construction	7	Construction – TBD	<p><u>Baxter Woodman</u> was awarded an agreement for construction, engineering and inspection services (CEI) for \$495,953.00</p> <p><u>Ric-Man</u> was awarded an agreement for general contractor construction services (GC) for \$4,056,327. - Commence construction: Mid July 2020. Project Status: <u>October Work Schedule:</u> -Final asphalt lift schedule at the end of October. -Contractor finishing punch list. Additional information is available on the website: http://osceolaparkproject.com/ Social Media Page Links Below: https://www.facebook.com/OsceolaPark/ https://twitter.com/osceola_park</p>

<p>NE 3rd Street Improvements <u>City Project #: 11-024</u> <u>CRA GL #: 5251</u></p>	<p>N/A</p>	<p>2</p>	<p>N/A</p>	<p>City is managing project. Coordination is ongoing. Job Order Contracting (JOC) is the preferred method to procure these services to streamline the process and complete the project efficiently. JOC is an approved method of public procurement and is available through the Sourcewell cooperative and ezIQ. Sourcewell is a national cooperative purchasing source solution and the City of Delray Beach has been a member since 2007. Additionally, ezIQ is one of the cooperative purchasing methods. The Gordian Group created ezIQ to make its industry-leading Job Order Contracting (JOC) solutions easily available through cooperative purchasing. JOC is an indefinite delivery/indefinite quantity procurement process that helps facility and infrastructure owners complete a large number of repairs, renovation and straightforward new construction projects with a single, competitively bid contract. Unlike traditional bidding where each project is identified, designed and then put out to bid, ezIQ establishes competitively bid prices up front and eliminates the need to bid each project separately. Sourcewell's procurement process satisfies the City's competitive bid requirements. The Gordian Group's expert field personnel guide owners through each step of the process, providing oversight to ensure cost and timing efficiencies are maximized right from the start. City is waiting for 100% design plans from consultant. Design-build went to City Commission: 5-4-21. Design Workshop Meeting with Parking Garage Project Team: 6-8-21. City issue NTP to DMSI for Design Phase (90 Days): 6-14-21. Public Outreach Meeting #1: 6-16-21. Public Outreach Meeting #2: 7-15-21. The 90% design plans were sent to the City on 9/15/2021. Preconstruction/Public outreach meeting on 9/23/21. Preconstruction meeting on October 21, 2021.</p>
<p>Wayfinding Signage <u>CRA GL #: 5236</u></p>	<p>Design & Implementation</p>	<p>1-3</p>	<p>N/A</p>	<p>On 4-27-21 the CRA Board Meeting approved an inter local agreement between the City and CRA. City staff is engaging a consultant to continue working on the project. City is negotiating SA with consultant for permits submittal to FDOT and construction services. Negotiating SA with consultant at this time. City processing PO with KH for permit with FDOT.</p>
<p>Pompey Park Master Plan <u>City Project #: 16-102</u> <u>CRA GL #: 5661</u></p>	<p>N/A</p>	<p>4</p>	<p>N/A</p>	<p>The City of Delray Beach's Parks and Recreation Department will be hosting a public meeting on 9-22-21. Updates on the progress of the Pompey Park Project, a review of the design, and additional information regarding the project will be available at the meeting. The project will be starting in October. Additional information is available on the website: http://pompeyparkproject.com</p>
